

**RECLAMATION DISTRICT NO. 1601
TWITCHELL ISLAND
BOARD OF TRUSTEES MEETING
TUESDAY, FEBRUARY 17, 2026
9:00 AM
ENGINEER'S REPORT**

I. PROJECT FUNDING AGREEMENT TW – 24 - 1.0 - SP PHASE II OF DISTRICT MULTI-BENEFIT PROJECT

- A. KSN Inc. is continuing to work on pre-construction submittals with Dutra Construction.
- B. KSN Inc. and PG&E have agreed on the design of the power pole alignment. KSN Inc. is preparing the necessary legal description and plat to accompany PG&E's easement deed language and will be seeking approval from DWR Real Estate Division.
- C. DSC Consistency Determination public review period has ended, and there were no official appeals filed.
- D. Construction is still anticipated to start in May 2026.

II. PROJECT FUNDING AGREEMENT TW – 21 - 1.2 TIMES/TWERP PROJECT

- A. Update on Irrigation and planting activity includes the planting is complete and the 3-year maintenance period has commenced.

EXHIBIT A: T&R Restore Progress Payment No. 3.

EXHIBIT B: T&R Restore Progress Payment No. 4.

- B. Update on plant procurement activity includes that the plant procurement is complete and the contract is finalized.

EXHIBIT C: The Watershed Nursery Progress Payment No. 3.

EXHIBIT D: T&R Restore The Watershed Nursery Progress Payment No. 4 & Release of Retention.

III. DISTRICT PUMP STATION SOLAR ARRAY

- A. PGE Interconnection

- a) Transformer & Switch Gear Location: – PG&E has finalized the requirements for the location of the Switchgear and pad mounted transformer.

- b) Update on transformer and switchgear foundation pad and fill design and construction.

EXHIBIT E: Transformer & Switch Gear Site Plan

EXHIBIT A



Progress Pay Estimate

No. 3

PROJECT: 1110-1010-13
TWERP Irrigation & Planting

DATE: 2/10/2026

CONTRACTOR: T&R Restore

CONTRACT ID: 1601-09-19-25-02

CONTRACT TIME:

Original Time 117 days
Notice to Proceed Date 10/6/2025
Original Completion Date 1/31/2026
Approved Time Extensions 0 days
Revised Completion Date 1/31/2026
Work Completed Through 12/31/2025
Elapsed Time 86 days
Percent Time Elapsed 73.5%

CONTRACT COST:

Original Contract Price \$1,491,401.50
Approved Change Orders \$35,242.94
Percent Change Orders 2.4%
Revised Contract Price \$1,526,644.44
Amount Complete to Date \$633,092.28
Percent Complete 41.5%

CURRENT PAYMENT SUMMARY:

DESCRIPTION	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
To Date	\$633,092.28	(\$31,654.61)	\$0.00	\$601,437.67
Previous	\$450,441.42	(\$22,522.07)	\$0.00	\$427,919.35
Current	\$182,650.86	(\$9,132.54)	\$0.00	\$173,518.32
Net Payment Due This Invoice:				\$173,518.32

OVERALL PAYMENT SUMMARY:

NO.	WORK COMPLETED THROUGH	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
1	10/31/2025	\$186,323.18	(\$9,316.16)	\$0.00	\$177,007.02
2	11/30/2025	\$264,118.24	(\$13,205.91)	\$0.00	\$250,912.33
3	12/31/2025	\$182,650.86	(\$9,132.54)	\$0.00	\$173,518.32
TOTALS:		\$633,092.28	(\$31,654.61)	\$0.00	\$601,437.67

NOTES:

SUPPORTING DOCUMENTATION
T&R Restore Invoice No. 1888 dated 1/5/2026 and Invoice No. 1892 dated 1/19/2026.

RECOMMENDED FOR PAYMENT
KSN, Inc. 
BY: Erik Almaas, PE Project Manager



PROJECT: 1110-1010-13
TWERP Irrigation & Planting
CONTRACTOR: T&R Restore

Progress Pay Estimate No. 3

DATE: 2/10/2026

CONTRACT ID: 1601-09-19-25-02

ITEM NO.	ITEM DESCRIPTION	UNIT	CONTRACT			TOTAL ESTIMATE TO DATE			PREVIOUS ESTIMATE			CURRENT ESTIMATE		
			QTY	UNIT PRICE	AMOUNT	QTY	%	AMOUNT	QTY	%	AMOUNT	QTY	%	AMOUNT
ORIGINAL CONTRACT														
SCHEDULE 1: GENERAL & IRRIGATION					\$1,491,401.50		40.09%	\$597,849.34		28.12%	\$419,317.42		11.97%	\$178,531.92
1	Mobilization	LS	1	\$73,562.50	\$73,562.50		50.00%	\$36,781.25		50.00%	\$36,781.25		7.45%	\$24,661.65
2	Site Preparation	LS	1	\$11,039.38	\$11,039.38		100.00%	\$11,039.38		100.00%	\$11,039.38			
3	Irrigation Installation	LS	1	\$246,616.51	\$246,616.51		100.00%	\$246,616.51		90.00%	\$221,954.86		10.00%	\$24,661.65
SCHEDULE 2: SEEDING					\$25,206.57		100.00%	\$25,206.57		100.00%	\$25,206.57		0.00%	\$0.00
1	Carex barbarae	LB	8	\$355.52	\$2,844.16	8	100.00%	\$2,844.16	8	100.00%	\$2,844.16			
2	Elymus glaucus	LB	42	\$76.59	\$3,216.78	42	100.00%	\$3,216.78	42	100.00%	\$3,216.78			
3	Elymus triticoides	LB	33	\$125.03	\$4,125.03	33	100.00%	\$4,125.99	33	100.00%	\$4,125.59			
4	Hordeum brachyantherum subsp. californicum	LB	59	\$111.31	\$6,567.29	59	100.00%	\$6,567.29	59	100.00%	\$6,567.29			
5	Junco bairdii	LB	11	\$338.75	\$3,726.25	11	100.00%	\$3,726.25	11	100.00%	\$3,726.25			
6	Poa secunda subsp. secunda	LB	4	\$242.67	\$971.48	4	100.00%	\$971.48	4	100.00%	\$971.48			
7	Stipa pulchra	LB	34	\$110.43	\$3,754.62	34	100.00%	\$3,754.62	34	100.00%	\$3,754.62			
SCHEDULE 3: PLANT INSTALLATION (CONTRACTOR FURNISHED)					\$240,949.06		66.35%	\$159,875.40		51.60%	\$124,335.36		14.75%	\$35,540.04
1	Baccharis salicifolia subsp. salicifolia	EA	2,170	\$10.64	\$23,068.80									
2	Populus fremontii subsp. fremontii	EA	749	\$13.26	\$9,931.74									
3	Salix exigua	EA	1,510	\$13.27	\$20,037.70									
4	Salix gooddingii	EA	278	\$14.32	\$3,980.96									
5	Salix laevigata	EA	160	\$19.08	\$3,052.80									
6	Salix lasiandra	EA	137	\$45.70	\$6,260.90									
7	Salix lasiolepis	EA	1,236	\$11.91	\$14,720.76									
8	Schoenoplectus californicus AND/OR	EA	49,536	\$2.51	\$124,335.36	49,536	100.00%	\$124,335.36	49,536	100.00%	\$124,335.36			
9	Quercus agrifolia	EA	2,202	\$10.34	\$22,768.68	2,202	100.00%	\$22,768.68				2,202	100.00%	\$22,768.68
10	Quercus lobata	EA	1,176	\$10.86	\$12,771.36	1,176	100.00%	\$12,771.36				1,176	100.00%	\$12,771.36
SCHEDULE 4: PLANT INSTALLATION (DISTRICT FURNISHED)					\$135,446.64		87.36%	\$118,330.23		0.00%	\$0.00		87.36%	\$118,330.23
1	Acer negundo	EA	506	\$12.54	\$6,345.24	755	149.21%	\$9,467.70				755	149.21%	\$9,467.70
2	Baccharis pilularis	EA	4,371	\$9.73	\$42,529.83	4,383	100.27%	\$42,646.59				4,383	100.27%	\$42,646.59
3	Cephalanthus occidentalis	EA	1,191	\$11.22	\$13,363.02									
4	Fraxinus latifolia	EA	474	\$17.05	\$8,081.70	483	101.90%	\$8,235.15				483	101.90%	\$8,235.15
5	Platanus racemosa	EA	1,216	\$12.09	\$14,701.44	595	48.93%	\$7,193.55				595	48.93%	\$7,193.55
6	Rosa californica	EA	1,408	\$11.27	\$15,868.16	1,410	100.14%	\$15,890.70				1,410	100.14%	\$15,890.70
7	Rubus ursinus	EA	444	\$14.00	\$6,216.00	450	101.35%	\$6,300.00				450	101.35%	\$6,300.00
8	Sambucus mexicana	EA	1,775	\$13.58	\$24,104.50	1,768	100.73%	\$24,281.04				1,768	100.73%	\$24,281.04
9	Vitis californica	EA	269	\$15.75	\$4,236.75	274	101.86%	\$4,315.50				274	101.86%	\$4,315.50
SCHEDULE 5: ESTABLISHMENT & MAINTENANCE PERIOD (3 YEARS)					\$758,580.84		0.00%	\$0.00		0.00%	\$0.00		0.00%	\$0.00
1	Plant Establishment and Maintenance - Year 1	LS	1	\$102,212.66	\$102,212.66									
2	Plant Establishment and Maintenance - Year 2	LS	1	\$103,765.66	\$103,765.66									
3	Plant Establishment and Maintenance - Year 3	LS	1	\$145,455.31	\$145,455.31									
4	Weed Management - Year 1	LS	1	\$153,397.17	\$153,397.17									
5	Weed Management - Year 2	LS	1	\$126,874.92	\$126,874.92									
6	Weed Management - Year 3	LS	1	\$126,874.92	\$126,874.92									
CHANGE ORDERS														
CO 001					\$35,242.94		100.00%	\$35,242.94		88.31%	\$31,124.00		11.69%	\$4,118.94
001-001	Schoenoplectus californicus AND/OR	EA	12,400	\$2.51	\$31,124.00	12,400	100.00%	\$31,124.00	12,400	100.00%	\$31,124.00		0.00%	\$0.00
CO 002					\$4,118.94		100.00%	\$4,118.94		0.00%	\$0.00		100.00%	\$4,118.94
002-001	Model 3 Pro Vac Slide Valve Pump	LS	1	\$4,118.94	\$4,118.94		100.00%	\$4,118.94					100.00%	\$4,118.94
TOTALS:					\$1,526,644.44		41.47%	\$633,092.28		29.51%	\$450,441.42		11.96%	\$182,650.86

T&R Restore

446 Market St
Colusa, CA 95932
+15306829299
rreynoso@trrestore.com



INVOICE

BILL TO
Reclamation District No. 1601 – Twitchell Island
2360 W. Twitchell Island Road
Rio Vista, CA 94571

INVOICE 1888
DATE 01/05/2026
TERMS Net 30
DUE DATE 02/04/2026

DATE	ITEM NUMBER	DESCRIPTION	QTY	UNIT PRICE	AMOUNT
12/31/2025	2540-Twitchell Island SHC1-Item 3 Irrigation Installation		0.10	246,616.51	24,661.65
12/31/2025	2540-Twitchell Island SHC3 Plant (CF) item 9	Quercus agrifolia	2,202	10.335881	22,759.61
12/31/2025	2540-Twitchell Island SHC3 Plant (CF) item 10	Quercus lobata	1,176	10.857534	12,768.46
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item 1	Acer negundo	755	12.544821 2	9,471.34
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item 2	Baccharis pilularis	4,383	9.7340657	42,664.41
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item 4	Fraxinus latifolia	483	17.046149 1	8,233.29
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item 5	Platanus racemosa	595	12.087630 3	7,192.14
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item 6	Rosa californica	1,410	11.268972	15,889.25
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item 7	Rubus ursinus	450	13.999921 5	6,299.96
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item 8	Sambucus mexicana	1,788	13.584814 5	24,289.65
12/31/2025	2540-Twitchell Island SHC4 Plant (DF) item	Vitis californica	274	15.754897 1	4,316.84

9

12/31/2025

Retention 5%

-1

8,927.33

-8,927.33

BALANCE DUE

\$169,619.27

INV + RETENTION

\$178,546.60

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 30, 2025

Daily Field Report
T&R Restore
5307131522

Weather



42°F

Precipitation: 0.0"
Wind: 5 mph
Humidity: 98%

8 AM



44°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 97%

12 PM



45°F

Precipitation: 0.0"
Wind: 4 mph
Humidity: 92%

5 PM

Source: Weather

Progress Summary

Laid all drip hose out planted plants and labeled understory



ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

7

INJURIES REPORTED

0

HOURS

56:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Amador Alcaraz	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Daniel Joseph Brunner	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Josue Joan Valadez	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Luis Velasquez	Yes	No	Yes	7:30 AM - 11:30 AM 12:00 PM - 4:00 PM	8:00
Miguel Nunez	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00
Vincent Ferrara	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	48:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
3	56:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM	Amador Alcaraz, Vincent Ferrara	16:00	---	16:00
2022 Chevrolet	Daniel Joseph Brunner, Josue Joan Valadez, Miguel Nunez, Nicholas Reynoso	32:00	---	32:00
2024 F250	Luis Velasquez, Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	20:00
2540-SHC4 Plant install (DF) item 1-9 Container	36:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/31/2025

Prepared by: Nicholas Reynoso

12/31/2025 @ 9:51 AM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 29, 2025

Daily Field Report
T&R Restore
5307131522

Weather



39°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 96%

8 AM



46°F

Precipitation: 0.0"
Wind: 5 mph
Humidity: 87%

12 PM



49°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 81%

5 PM

Source: Weather

Progress Summary

Laid irrigation and label understory

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

7

INJURIES REPORTED

0

HOURS

50:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Amador Alcaraz	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Daniel Joseph Brunner	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:30 AM - 12:30 PM 12:30 PM - 4:00 PM	8:00
Luis Velasquez	Yes	No	Yes	7:30 AM - 9:30 AM	2:00
Miguel Nunez	---	---	---	7:30 AM - 12:00 PM 12:30 PM - 4:00 PM	8:00
Nicholas Reynoso	Yes	No	Yes	7:30 AM - 8:30 AM (-0:30) 8:30 AM - 4:00 PM	8:00
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	47:00
2540 - Mgmt. ---	3:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	2:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250	Luis Velasquez	2:00	---	2:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	27:00
2540-SHC4 Plant install (DF) item 1-9 Container	23:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/30/2025

Prepared by: Nicholas Reynoso

12/30/2025 @ 7:32 AM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 19, 2025

Daily Field Report
T&R Restore
5307131522

Weather



51°F

Precipitation: 0.0"
Wind: 10 mph
Humidity: 96%

8 AM



56°F

Precipitation: 0.0"
Wind: 12 mph
Humidity: 89%

12 PM



57°F

Precipitation: <.05"
Wind: 8 mph
Humidity: 92%

5 PM

Source: Apple Weather

Progress Summary

Moving plants and labels

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

5

INJURIES REPORTED

0

HOURS

33:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Daniel Joseph Brunner	---	---	---	(-0:30) 7:00 AM - 3:00 PM	7:30
Katie Jacobs	Yes	No	Yes	(-0:30) 10:00 AM - 1:30 PM	3:00
Miguel Nunez	---	---	---	(-0:30) 7:00 AM - 3:00 PM	7:30
Nicholas Reynoso	---	---	---	7:00 AM - 9:00 AM (-0:30) 9:00 AM - 3:00 PM	7:30
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:00 AM - 3:00 PM	7:30

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	28:00
2540 - Mgmt. ---	3:00
2540-Operator ---	2:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
2	4:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2022 Chevrolet ---	Nicholas Reynoso	---	2:00	2:00
Case 90 ---	Nicholas Reynoso	2:00	---	2:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 2 Site Preparation	2:00
2540-SHC4 Plant install (DF) item 1-9 Container	31:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☒	---
Amount	☐	☐	☒	---

Sign-Off

Vincent Ferrara

12/19/2025

Prepared by: Vincent Ferrara

12/19/2025 @ 3:47 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Daily Field Report
T&R Restore
5307131522

Project #: 2540
Dec 18, 2025

Progress Summary

Mowed grass where plants are going in scrub shrub planting areas and put out labels

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

24:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Daniel Joseph Brunner	Yes	No	Yes	7:00 AM - 11:00 AM	4:00
Miguel Nunez	Yes	No	Yes	7:00 AM - 11:00 AM	4:00
Nicholas Reynoso	Yes	No	Yes	7:00 AM - 10:30 AM (-0:30) 10:30 AM - 3:30 PM	8:00

Vincent Ferrara

Yes

No

Yes

(-0:30) 7:00 AM - 3:30 PM

8:00

Cost Code Summary

Cost Code

Hours

2540 - Labor

19:30

2540-Operator

4:30

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	3:30

Name

Operator

Labor Hrs

Add-On Hrs

Total Hrs

2022 Chevrolet

Nicholas Reynoso

3:30

3:30

Subproject Summary

Subprojects

Hours

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/18/2025

2540 - Twitchell Island Wetland Enhancement (TWERP) / 2540-SHC3
Plant Install (CF) item 9 -10 Acorns

Dec 17, 2025

Daily Field
Report
T&R
Restore
530-713-
1522

WEATHER



47°F

8 AM

Precipitation: <.05"
Wind: 9 mph
Humidity: 99%



56°F

12 PM

Precipitation: 0.0"
Wind: 7 mph
Humidity: 94%



61°F

5 PM

Precipitation: 0.0"
Wind: 4 mph
Humidity: 88%

Sourced by Weather

PROGRESS SUMMARY

finished planted acorns

EMPLOYEE SUMMARY

EMPLOYEES ON SITE

6

INJURIES REPORTED

0

TOTAL HOURS

25:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Daniel Joseph Brunner	Yes	No	Yes	7:00 AM – 11:00 AM	04:00
Josue Joan Valadez	---	---	---	7:00 AM – 11:00 AM	04:00
Luis Velasquez	Yes	No	Yes	7:00 AM – 12:00 PM	05:00
Martin Alcaraz	---	---	---	7:00 AM – 11:00 AM	04:00

Miguel Nunez	---	---	---	7:00 AM – 11:00 AM	04:00
Pedro Corona Jr.	---	---	---	7:00 AM – 11:00 AM	04:00

COST CODE SUMMARY

Cost Code	Hours
2540 - Labor	20:00
2540 - Mgmt.	05:00

EQUIPMENT SUMMARY

MACHINES ON SITE	TOTAL HOURS
1	05:00

Name	Operator	Labor Hrs
2024 F250 unknown unknown	Luis Velasquez	05:00

SUBPROJECT SUMMARY

NO DATA

HERBICIDE USAGE

HERBICIDE

Question	Yes	No	N/A	Description
Rate				
Amount				

SIGN-OFF

Click to Sign

Luis Velasquez 12/17/2025

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 17, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Planted acorns

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

7

INJURIES REPORTED

0

HOURS

29:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Daniel Joseph Brunner	---	---	---	7:00 AM - 11:00 AM	4:00
Josue Joan Valadez	---	---	---	7:00 AM - 11:00 AM	4:00
Luis Velasquez	Yes	No	Yes	7:00 AM - 12:00 PM	5:00

Martin Alcaraz	---	---	---	7:00 AM - 11:00 AM	4:00
Miguel Nunez	---	---	---	7:00 AM - 11:00 AM	4:00
Nicholas Reynoso	Yes	No	Yes	7:00 AM - 10:30 AM 10:30 AM - 11:30 AM	4:30
Pedro Corona Jr.	---	---	---	7:00 AM - 11:00 AM	4:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	23:30
2540 - Mgmt. ---	6:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	5:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250 ---	Luis Velasquez	5:00	---	5:00

Subproject Summary

Subprojects	Hours
2540-SHC3 Plant Install (CF) item 9 -10 Acorns	25:00
2540-SHC4 Plant install (DF) item 1-9 Container	4:30

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 16, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Finished container planting started with acorns

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

8

INJURIES REPORTED

0

HOURS

63:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Andres Navarro	---	---	---	7:00 AM - 2:00 PM 2:00 PM - 3:30 PM	8:30
Jose Velazquez G	---	---	---	(-0:30) 7:00 AM - 2:00 PM 2:00 PM - 3:30 PM	8:00

Josue Joan Valadez	---	---	---	7:00 AM - 2:00 PM 2:00 PM - 3:30 PM	8:30
Luis Velasquez	Yes	No	Yes	7:00 AM - 11:00 AM 11:30 AM - 1:30 PM	6:00
Miguel Nunez	---	---	---	(-0:30) 7:00 AM - 2:00 PM 2:00 PM - 3:30 PM	8:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Pedro Corona Jr.	---	---	---	(-0:30) 7:00 AM - 2:00 PM 2:00 PM - 3:30 PM	8:00
Vincent Ferrara	---	---	---	7:00 AM - 2:00 PM 2:00 PM - 3:30 PM	8:30

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	57:30
2540 - Mgmt. ---	6:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	4:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250 ---	Luis Velasquez	4:00	---	4:00

Subproject Summary

Subprojects	Hours
2540-SHC3 Plant Install (CF) item 9 -10 Acorns	11:00
2540-SHC4 Plant install (DF) item 1-9 Container	52:30

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/17/2025

Prepared by: Nicholas Reynoso

12/17/2025 @ 5:41 AM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 15, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Started to plant acorns and planted container plants

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

9

INJURIES REPORTED

0

HOURS

71:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Andres Navarro	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Daniel Joseph Brunner	Yes	No	Yes	7:00 AM - 10:30 AM (-0:30) 10:30 AM - 3:30 PM	8:00
Jose Velazquez G	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00

Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Miguel Nunez	Yes	No	Yes	(-0:30) 8:30 AM - 4:00 PM	7:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Pedro Corona Jr.	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Vincent Ferrara	Yes	No	Yes	7:00 AM - 9:00 AM (-0:30) 9:00 AM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	63:00
2540 - Mgmt. ---	8:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
2	16:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2022 Chevrolet ---	Nicholas Reynoso	8:00	---	8:00
2024 F250 ---	Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC3 Plant Install (CF) item 9 -10 Acorns	10:30
2540-SHC4 Plant install (DF) item 1-9 Container	60:30

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---



Nicholas Reynoso

12/15/2025

Prepared by: Nicholas Reynoso

12/15/2025 @ 8:37 PM

Generated by:

 **BusyBusy**

www.bsybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 12, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Planted plants and continued with labeling

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE
10

INJURIES REPORTED
0

HOURS
80:00

Employee	Correct	Time Injured	Break Compliance	Entries	Hours
Andres Navarro	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Daniel Joseph Brunner	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Edgar Sainz	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00

Jesus Hernandez Flores	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Jose Velazquez G	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Miguel Nunez	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Pedro Corona Jr.	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	72:00
2540 - Mgmt.	8:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
2	16:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM ---	Josue Joan Valadez	8:00	---	8:00
2024 F250 ---	Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC4 Plant install (DF) item 1-9 Container	80:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/15/2025

Prepared by: Nicholas Reynoso

12/15/2025 @ 4:27 AM

Generated by:



www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 12, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Planted trees and finished labeling

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE
11

INJURIES REPORTED
0

HOURS
88:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Andres Navarro	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Daniel Joseph Brunner	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Edgar Sainz	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00

Jesus Hernandez Flores	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Jose Velazquez G	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Miguel Nunez	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Pedro Corona Jr.	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Vincent Ferrara	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	80:00
2540 - Mgmt.	8:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
2	16:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM ---	Josue Joan Valadez	8:00	---	8:00
2024 F250 ---	Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC4 Plant install (DF) item 1-9 Container	88:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/15/2025

Prepared by: Nicholas Reynoso

12/15/2025 @ 10:06 AM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 11, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Planted plants and got the pump running and put out labels

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

11

INJURIES REPORTED

0

HOURS

88:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Andres Navarro	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Daniel Joseph Brunner	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Edgar Sainz	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00

Jesus Hernandez Flores	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Jose Velazquez G	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Josue Joan Valadez	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Katie Jacobs	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Miguel Nunez	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Pedro Corona Jr.	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	72:00
2540 - Mgmt. ---	16:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
2	16:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM ---	Pedro Corona Jr.	8:00	---	8:00
2024 F250 ---	Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	8:00
2540-SHC4 Plant install (DF) item 1-9 Container	80:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/12/2025

Prepared by: Nicholas Reynoso

12/12/2025 @ 5:18 AM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 10, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Started to plant plants and continued with labeling

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

8

INJURIES REPORTED

0

HOURS

58:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Daniel Joseph Brunner	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Edgar Sainz	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00

Luis Velasquez	---	---	---	(-0:30) 8:00 AM - 4:30 PM	8:00
Miguel Nunez	---	---	---	(-0:30) 8:30 AM - 4:00 PM	7:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 12:00 PM - 3:30 PM	3:00
Pedro Corona Jr.	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Vincent Ferrara	---	---	---	(-0:30) 7:00 AM - 2:30 PM 2:30 PM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	49:00
2540 - Mgmt.	9:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	8:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
------	----------	-----------	------------	-----------

Subproject Summary

Subprojects

Hours

2540-SHC4 Plant install (DF) item 1-9 Container

58:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



2540 - Twitchell Island Wetland Enhancement (TWERP)

Daily Field Report
T&R Restore
5307131522

Project #: 2540
Dec 09, 2025

Progress Summary

Labeled and put marked out planting areas

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

8

INJURIES REPORTED

0

HOURS

64:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Daniel Joseph Brunner	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Edgar Sainz	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Josue Joan Valadez	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00

Katie Jacobs	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Nicholas Reynoso	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Pedro Corona Jr.	---	---	---	(-0:30) 7:00 AM - 3:30 PM	8:00
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:30 AM - 12:30 PM 12:30 PM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	48:00
2540 - Mgmt.	16:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
3	24:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
------	----------	-----------	------------	-----------

2022 Chevrolet ---	Nicholas Reynoso	8:00	---	8:00
2024 F250 ---	Luis Velasquez	8:00	---	8:00
Personal Vehicle ---	Katie Jacobs	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	4:30
2540-SHC4 Plant install (DF) item 1-9 Container	51:30

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---



Nicholas Reynoso

12/10/2025

Prepared by: Nicholas Reynoso

12/10/2025 @ 6:20 AM

Generated by:



www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Daily Field Report
T&R Restore
5307131522

Project #: 2540
Dec 08, 2025

Progress Summary

Button up rest of irrigation and fixed lines and started to label

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE	INJURIES REPORTED	HOURS
7	0	56:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Daniel Joseph Brunner	---	---	---	7:30 AM - 12:30 PM (-0:30) 12:30 PM - 4:00 PM	8:00
Edgar Sainz	---	---	---	(-0:30) 7:30 AM - 12:30 PM 12:30 PM - 4:00 PM	8:00

Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:30 AM - 12:30 PM 12:30 PM - 4:00 PM	8:00
Kristina Alvarez	---	---	---	8:00 AM - 4:00 PM	8:00
Luis Velasquez	---	---	---	(-0:30) 7:30 AM - 12:30 PM 12:30 PM - 4:00 PM	8:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:30 AM - 12:30 PM 12:30 PM - 4:00 PM	8:00
Vincent Ferrara	Yes	No	Yes	7:30 AM - 12:30 PM (-0:30) 12:30 PM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	40:00
2540 - Mgmt. ---	16:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
3	15:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM ---	Luis Velasquez, Luis Velasquez	8:00	---	8:00
2022 Chevrolet ---	Nicholas Reynoso	---	3:30	3:30
Side-by-side POLARIS XPEDITION	Nicholas Reynoso	3:30	---	3:30

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 2 Site Preparation	8:00
2540-SHC1-Item 3 Irrigation Installation	28:00
2540-SHC4 Plant install (DF) item 1-9 Container	20:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/08/2025

Prepared by: Nicholas Reynoso

12/08/2025 @ 5:27 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 05, 2025

Daily Field Report
T&R Restore
5307131522

Weather



39°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 98%

8 AM



41°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 97%

12 PM



42°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 97%

5 PM

Source: Apple Weather

Progress Summary

Setting up filter and pump

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

29:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	---	---	---	(-0:30) 7:00 AM - 6:00 PM	10:30
Luis Velasquez	Yes	No	Yes	12:30 PM - 3:30 PM	3:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:00 AM - 1:00 PM	5:30
Vincent Ferrara	---	---	---	(-0:30) 7:00 AM - 6:00 PM	10:30

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	26:30
2540 - Mgmt. ---	3:00

Equipment Summary

MACHINES ON SITE

2

TOTAL HOURS

8:30

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
------	----------	-----------	------------	-----------

2022 Chevrolet ---	Nicholas Reynoso	5:30	---	5:30
2024 F250 ---	Luis Velasquez	3:00	---	3:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	29:30

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☒	---
Amount	☐	☐	☒	---

Vincent F

Vincent Ferrara

12/06/2025

Prepared by: Vincent Ferrara

12/06/2025 @ 8:21 AM

Generated by:



www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 04, 2025

Daily Field Report
T&R Restore
5307131522

Weather



45°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 91%

8 AM



47°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 85%

12 PM



47°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 87%


5 PM

Source: Apple Weather

Progress Summary

Spraying and irrigating

ADDITIONAL PHOTOS

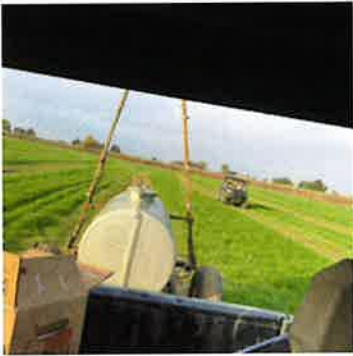

Employee Summary

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

25:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	7:00 AM - 9:30 AM (-0:30) 9:30 AM - 3:30 PM 3:30 PM - 4:15 PM	8:45
Nicholas Reynoso	Yes	No	Yes	7:00 AM - 10:00 AM (-0:30) 10:00 AM - 3:30 PM	8:00
Vincent Ferrara	---	---	---	7:00 AM - 9:30 AM (-0:30) 9:30 AM - 4:15 PM	8:45

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	10:30
2540-Operator ---	7:00
2540-Transportation ---	8:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	12:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
Side-by-side POLARIS XPEDITION	Josue Joan Valadez, Nicholas Reynoso, Vincent Ferrara	12:00	---	12:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 2 Site Preparation	5:00
2540-SHC1-Item 3 Irrigation Installation	13:30
2540-SHC5-Weed Management – Year 1	7:00

Herbicide Usage

Honcho
Patrol

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Vincent F

Vincent Ferrara

12/05/2025

Prepared by: Vincent Ferrara

12/05/2025 @ 9:51 AM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Dec 03, 2025

Daily Field Report
T&R Restore
5307131522

Progress Summary

Mowed areas and installed irrigation parts along with receiving plant order 25 sycamores were not to healthy from nursery

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE	INJURIES REPORTED	HOURS
3	0	21:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
----------	--------------	---------	------------------	---------	-------

Josue Joan Valadez	---	---	---	7:00 AM - 9:30 AM (-0:30) 9:30 AM - 3:30 PM	8:00
Nicholas Reynoso	Yes	No	Yes	7:00 AM - 9:00 AM 9:00 AM - 10:30 AM (-0:30) 10:30 AM - 1:00 PM	5:30
Vincent Ferrara	---	---	---	7:00 AM - 9:30 AM (-0:30) 9:30 AM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	12:30
2540 - Mgmt. ---	2:00
2540-Operator ---	2:00
2540-Transportation ---	5:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	2:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
Case 90	Nicholas Reynoso	---	2:00	2:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	19:30
2540-SHC4 Plant install (DF) item 1-9 Container	2:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/04/2025

Prepared by: Nicholas Reynoso

12/04/2025 @ 8:50 AM

Generated by:

 **BusyBusy**

www.busybusy.com

Progress Summary

Sprayed and set filters

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE	INJURIES REPORTED	HOURS
2	0	16:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Nicholas Reynoso	Yes	No	Yes	7:00 AM - 11:30 AM (-0:30) 11:30 AM - 3:30 PM	8:00
Vincent Ferrara	---	---	---	7:00 AM - 9:00 AM 9:00 AM - 11:00 AM (-0:30) 11:00 AM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	3:30
2540 - Mgmt. ---	4:30
2540 - Off Site Labor ---	2:00
2540-Operator ---	4:00
2540-Transportation ---	2:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	7:30

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
Side-by-side POLARIS XPEDITION	Nicholas Reynoso, Vincent Ferrara	7:30	---	7:30

Subproject Summary

Subprojects

Hours

2540-SHC4 Plant install (DF) item 1-9 Container

8:00

2540-SHC5-Weed Management – Year 1

8:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

12/03/2025

T&R Restore

446 Market St
Colusa, CA 95932
+15306829299
rreynoso@trrestore.com

**INVOICE**

BILL TO
Reclamation District No. 1601 – Twitchell Island
2360 W. Twitchell Island Road
Rio Vista, CA 94571

INVOICE 1892
DATE 01/19/2026
TERMS Net 30
DUE DATE 02/18/2026

DATE	ITEM NUMBER	DESCRIPTION	QTY	UNIT PRICE	AMOUNT
12/31/2025	2540-Twitchell Island Contractors Fee	MODEL 3 PRO VAC SLIDE VALVE PUMP	1	3,581.69	3,581.69
12/31/2025	2540-Twitchell Island Material Mark-up	Per 11.7.C.2a	1	537.25	537.25

BALANCE DUE

\$4,118.94



0203675
12/16/2025

TOICO Industries, Inc.
3205 South Bouwhuis Drive
West Haven, UT 84401
(888) 935-1133

1834
0117533

TimePayment Corporation
200 SUMMIT DR
BURLINGTON, MA 01803-5264

T&R Restore
446 MARKET ST
COLUSA, CA 95932-2424

Ruben Reynoso

Quote - App ID: 5055975

Credit Card

Item	Bin	EA	1.0000	0.0000	1.0000	3,131.6900	3,131.69
ADUN03PV05ES							
MODEL 3 PRO VAC SLIDE VALVE UN							
Whse: 001							
3 day lead time							
Shipping \$450							

per. 11.7. C. 2a

cost + 15%

Net Order:	3,131.69
Less Discount:	0.00
Freight:	450.00
Sales Tax:	0.00
	3,581.69

EXHIBIT B



Progress Pay Estimate

No. 4

PROJECT: 1110-1010-13
TWERP Irrigation & Planting

DATE: 2/10/2026

CONTRACTOR: T&R Restore

CONTRACT ID: 1601-09-19-25-02

CONTRACT TIME:

Original Time 117 days
Notice to Proceed Date 10/6/2025
Original Completion Date 1/31/2026
Approved Time Extensions 0 days
Revised Completion Date 1/31/2026
Work Completed Through 1/31/2026
Elapsed Time 117 days
Percent Time Elapsed 100.0%

CONTRACT COST:

Original Contract Price \$1,491,401.50
Approved Change Orders \$35,242.94
Percent Change Orders 2.4%
Revised Contract Price \$1,526,644.44
Amount Complete to Date \$714,165.94
Percent Complete 46.8%

CURRENT PAYMENT SUMMARY:

DESCRIPTION	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
To Date	\$714,165.94	(\$35,708.30)	\$0.00	\$678,457.64
Previous	\$633,092.28	(\$31,654.61)	\$0.00	\$601,437.67
Current	\$81,073.66	(\$4,053.68)	\$0.00	\$77,019.98
Net Payment Due This Invoice:				\$77,019.98

OVERALL PAYMENT SUMMARY:

NO.	WORK COMPLETED THROUGH	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
1	10/31/2025	\$186,323.18	(\$9,316.16)	\$0.00	\$177,007.02
2	11/30/2025	\$264,118.24	(\$13,205.91)	\$0.00	\$250,912.33
3	12/31/2025	\$182,650.86	(\$9,132.54)	\$0.00	\$173,518.32
4	1/31/2026	\$81,073.66	(\$4,053.68)	\$0.00	\$77,019.98
TOTALS:		\$714,165.94	(\$35,708.30)	\$0.00	\$678,457.64

NOTES:

SUPPORTING DOCUMENTATION
T&R Restore Invoice No. 1897 dated 2/4/2026.

RECOMMENDED FOR PAYMENT
KSN, Inc.
BY: Erik Almaas, PE Project Manager



PROJECT: 1110-1010-13
TWERP Irrigation & Planting

CONTRACTOR: T&R Restore

Progress Pay Estimate No. 4

DATE: 2/10/2026

CONTRACT ID: 1601-09-19-25-02

ITEM NO.	ITEM DESCRIPTION	UNIT	CONTRACT			TOTAL ESTIMATE TO DATE			PREVIOUS ESTIMATE			CURRENT ESTIMATE		
			QTY	UNIT PRICE	AMOUNT	QTY	%	AMOUNT	QTY	%	AMOUNT	QTY	%	AMOUNT
ORIGINAL CONTRACT														
SCHEDULE 1: GENERAL & IRRIGATION					\$1,491,401.50			\$678,923.00			\$592,849.34			\$81,073.66
1	Mobilization	LS	1	\$73,562.50	\$73,562.50		50.00%	\$36,781.25		50.00%	\$36,781.25		0.00%	\$0.00
2	Site Preparation	LS	1	\$11,039.38	\$11,039.38		100.00%	\$11,039.38		100.00%	\$11,039.38			
3	Irrigation Installation	LS	1	\$246,616.51	\$246,616.51		100.00%	\$246,616.51		100.00%	\$246,616.51			
SCHEDULE 2: SEEDING					\$25,206.57		100.00%	\$25,206.57		100.00%	\$25,206.57		0.00%	\$0.00
1	Carex barbarae	LB	8	\$355.52	\$2,844.16	8	100.00%	\$2,844.16	8	100.00%	\$2,844.16			
2	Elymus glaucus	LB	42	\$76.59	\$3,216.78	42	100.00%	\$3,216.78	42	100.00%	\$3,216.78			
3	Elymus tritoides	LB	33	\$125.03	\$4,125.99	33	100.00%	\$4,125.99	33	100.00%	\$4,125.99			
4	Hordeum brachyantherum subsp. californicum	LB	59	\$111.31	\$6,567.29	59	100.00%	\$6,567.29	59	100.00%	\$6,567.29			
5	Juncus balticus	LB	11	\$338.75	\$3,726.25	11	100.00%	\$3,726.25	11	100.00%	\$3,726.25			
6	Poa secunda subsp. secunda	LB	4	\$242.87	\$971.48	4	100.00%	\$971.48	4	100.00%	\$971.48			
7	Stipa pulchra	LB	34	\$110.43	\$3,754.62	34	100.00%	\$3,754.62	34	100.00%	\$3,754.62			
SCHEDULE 3: PLANT INSTALLATION (CONTRACTOR FURNISHED)					\$240,949.06		100.00%	\$240,949.06		66.35%	\$159,075.40		33.65%	\$81,073.66
1	Baccharis salicifolia subsp. salicifolia	EA	2,170	\$10.64	\$23,088.80	2,170	100.00%	\$23,088.80				2,170	100.00%	\$23,088.80
2	Populus fremontii subsp. fremontii	EA	749	\$13.26	\$9,931.74	749	100.00%	\$9,931.74				749	100.00%	\$9,931.74
3	Salix exigua	EA	1,510	\$13.27	\$20,037.70	1,510	100.00%	\$20,037.70				1,510	100.00%	\$20,037.70
4	Salix goodingii	EA	278	\$14.32	\$3,980.96	278	100.00%	\$3,980.96				278	100.00%	\$3,980.96
5	Salix laevigata	EA	160	\$19.08	\$3,052.80	160	100.00%	\$3,052.80				160	100.00%	\$3,052.80
6	Salix lasiandra	EA	137	\$45.70	\$6,260.90	137	100.00%	\$6,260.90				137	100.00%	\$6,260.90
7	Salix lasiolepis	EA	1,236	\$11.91	\$14,720.76	1,236	100.00%	\$14,720.76				1,236	100.00%	\$14,720.76
8	Schoenoplectus californicus AND/OR Schoenoplectus acutus subsp. occidentalis	EA	49,536	\$2.51	\$124,335.36	49,536	100.00%	\$124,335.36	49,536	100.00%	\$124,335.36			
9	Quercus agrifolia	EA	2,202	\$10.34	\$22,768.68	2,202	100.00%	\$22,768.68	2,202	100.00%	\$22,768.68			
10	Quercus lobata	EA	1,176	\$10.86	\$12,771.36	1,176	100.00%	\$12,771.36	1,176	100.00%	\$12,771.36			
SCHEDULE 4: PLANT INSTALLATION (DISTRICT FURNISHED)					\$105,446.64		87.36%	\$118,330.23		87.36%	\$118,330.23		0.00%	\$0.00
1	Acer negundo	EA	506	\$12.54	\$6,345.24	755	149.21%	\$9,467.70	755	149.21%	\$9,467.70			
2	Baccharis pilularis	EA	4,371	\$9.73	\$42,529.83	4,383	100.27%	\$42,646.59	4,383	100.27%	\$42,646.59			
3	Cephalanthus occidentalis	EA	1,191	\$11.22	\$13,363.02									
4	Fraxinus latifolia	EA	474	\$17.05	\$8,081.70	483	101.90%	\$8,235.15	483	101.90%	\$8,235.15			
5	Platanus racemosa	EA	1,216	\$12.09	\$14,701.44	595	48.93%	\$7,193.55	595	48.93%	\$7,193.55			
6	Rosa californica	EA	1,408	\$11.27	\$15,868.16	1,410	100.14%	\$15,890.70	1,410	100.14%	\$15,890.70			
7	Rubus ursinus	EA	444	\$14.00	\$6,216.00	450	101.35%	\$6,300.00	450	101.35%	\$6,300.00			
8	Sambucus mexicana	EA	1,775	\$13.58	\$24,104.50	1,788	100.73%	\$24,281.04	1,788	100.73%	\$24,281.04			
9	Vitis californica	EA	269	\$15.75	\$4,236.75	274	101.86%	\$4,315.50	274	101.86%	\$4,315.50			
SCHEDULE 5: ESTABLISHMENT & MAINTENANCE PERIOD (3 YEARS)					\$758,580.84		0.00%	\$0.00		0.00%	\$0.00		0.00%	\$0.00
1	Plant Establishment and Maintenance - Year 1	LS	1	\$102,212.66	\$102,212.66									
2	Plant Establishment and Maintenance - Year 2	LS	1	\$103,765.86	\$103,765.86									
3	Plant Establishment and Maintenance - Year 3	LS	1	\$145,455.31	\$145,455.31									
4	Weed Management - Year 1	LS	1	\$153,397.17	\$153,397.17									
5	Weed Management - Year 2	LS	1	\$126,874.92	\$126,874.92									
6	Weed Management - Year 3	LS	1	\$126,874.92	\$126,874.92									
CHANGE ORDERS														
CO 001					\$35,242.94		100.00%	\$35,242.94		100.00%	\$35,242.94		0.00%	\$0.00
001-001	Schoenoplectus californicus AND/OR Schoenoplectus acutus subsp. occidentalis	EA	12,400	\$2.51	\$31,124.00	12,400	100.00%	\$31,124.00	12,400	100.00%	\$31,124.00		0.00%	\$0.00
CO 002					\$4,118.94		100.00%	\$4,118.94		100.00%	\$4,118.94		0.00%	\$0.00
002-001	Model 3 Pro Vac Slide Valve Pump	LS	1	\$4,118.94	\$4,118.94		100.00%	\$4,118.94		100.00%	\$4,118.94			
TOTALS:					\$1,526,644.44		46.78%	\$714,165.94		41.47%	\$633,092.28		5.31%	\$81,073.66

T&R Restore

446 Market St
 Colusa, CA 95932
 +15306829299
 rreynoso@trrestore.com

**INVOICE**

BILL TO
 Reclamation District No. 1601 – Twitchell Island
 2360 W. Twitchell Island Road
 Rio Vista, CA 94571

INVOICE 1897
 DATE 02/04/2026
 TERMS Net 30
 DUE DATE 03/06/2026

DATE	ITEM NUMBER	DESCRIPTION	QTY	UNIT PRICE	AMOUNT
01/31/2026	2540-Twitchell Island SHC3 Plant (CF) item 1	Baccharis salicifolia subsp.salicifolia	2,170	10.641110 6	23,091.21
01/31/2026	2540-Twitchell Island SHC3 Plant (CF) item 2	Populus fremontii subsp. fremontii	749	13.258397 9	9,930.54
01/31/2026	2540-Twitchell Island SHC3 Plant (CF) item 3	Salix exigua	1,510	13.269761 6	20,037.34
01/31/2026	2540-Twitchell Island SHC3 Plant (CF) item 4	Salix gooddingii	278	14.315539 6	3,979.72
01/31/2026	2540-Twitchell Island SHC3 Plant (CF) item 5	Salix laevigata	160	19.078625	3,052.58
01/31/2026	2540-Twitchell Island SHC3 Plant (CF) item 6	Salix lasiandra	137	45.698613 1	6,260.71
01/31/2026	2540-Twitchell Island SHC3 Plant (CF) item 7	Salix lasiolepis	1,236	11.913559 9	14,725.16
01/31/2026	Retention 5%		-1	4,053.86	-4,053.86

BALANCE DUE

\$77,023.40

INV + RETENTION

\$81,077.26

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 08, 2026

Daily Field Report
T&R Restore
5307131522

Weather



43°F

8 AM

Precipitation: 0.0"
Wind: 4 mph
Humidity: 78%



54°F

12 PM

Precipitation: 0.0"
Wind: 15 mph
Humidity: 49%



50°F

5 PM


Precipitation: 0.0"
Wind: 12 mph
Humidity: 60%

Source: Apple Weather

Progress Summary

Finished the irrigation lines and started to collect cuttings

ADDITIONAL PHOTOS

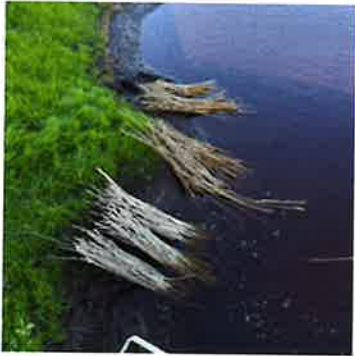

Employee Summary

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

32:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	7:30 AM - 11:30 AM (-0:30) 11:30 AM - 4:00 PM	8:00
Luis Velasquez	Yes	No	Yes	7:30 AM - 11:30 AM 12:00 PM - 4:00 PM	8:00
Nicholas Reynoso	Yes	No	Yes	7:30 AM - 11:30 AM (-0:30) 11:30 AM - 4:00 PM	8:00
Vincent Ferrara	---	---	---	7:30 AM - 11:30 AM (-0:30) 11:30 AM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	20:00
2540 - Off Site Labor ---	12:00

Equipment Summary

MACHINES ON SITE

1

TOTAL HOURS

8:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250	Luis Velasquez, Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	16:00
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	16:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---



Nicholas Reynoso

01/08/2026

Prepared by: Nicholas Reynoso

01/08/2026 @ 4:06 PM

Generated by:

 **BusyBusy**

www.bsybybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 12, 2026

Daily Field Report
T&R Restore
5307131522

Weather



36°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 96%

8 AM



52°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 80%

12 PM



54°F

Precipitation: 0.0"
Wind: 4 mph
Humidity: 78%

5 PM

Source: Apple Weather

Progress Summary

Collected cuttings offsite

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

32:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	16:00
2540 - Off Site Labor	16:00

Equipment Summary

MACHINES ON SITE

2

TOTAL HOURS

16:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
------	----------	-----------	------------	-----------

2022 Chevrolet ---	Nicholas Reynoso	8:00	---	8:00
2024 F250 ---	Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	16:00
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	16:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---



Nicholas Reynoso

01/12/2026

Prepared by: Nicholas Reynoso

01/12/2026 @ 3:43 PM

Generated by:

 **BusyBusy**

www.bsybybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 09, 2026

Daily Field Report
T&R Restore
5307131522

Weather



41°F

Precipitation: 0.0"
Wind: 1 mph
Humidity: 75%

8 AM



50°F

Precipitation: 0.0"
Wind: 7 mph
Humidity: 56%

12 PM



50°F

Precipitation: 0.0"
Wind: 4 mph
Humidity: 62%

5 PM

Source: Weather

Progress Summary

Collecting cuttings

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

25:00

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Katie Jacobs	Yes	No	Yes	2:30 PM - 3:30 PM	1:00
Nicholas Reynoso	---	---	---	(-0:30) 7:30 AM - 4:00 PM	8:00
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	8:00
2540 - Mgmt. ---	1:00
2540 - Off Site Labor ---	16:00

Equipment Summary

NO DATA

Subproject Summary

Subprojects

Hours

2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings

25:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☒	---
Amount	☐	☐	☒	---

Sign-Off



Vincent Ferrara

01/09/2026

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 13, 2026

Daily Field Report
T&R Restore
5307131522

Weather



35°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 97%

8 AM



48°F

Precipitation: 0.0"
Wind: 1 mph
Humidity: 98%

12 PM



53°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 76%

5 PM

Source: Apple Weather

Progress Summary

Collected cuttings and started some planting

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

25:19

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	7:30 AM - 10:30 AM 10:30 AM - 12:00 PM 12:00 PM - 4:01 PM	8:31
Nicholas Reynoso	Yes	No	Yes	7:30 AM - 10:30 AM 10:30 AM - 12:00 PM 12:10 PM - 4:01 PM	8:21
Vincent Ferrara	Yes	No	Yes	7:30 AM - 10:30 AM 10:30 AM - 12:00 PM 12:00 PM - 3:57 PM	8:27

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	18:28
2540 - Off Site Labor ---	6:51

Equipment Summary

NO DATA

Subproject Summary

Subprojects	Hours
-------------	-------

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso01/13/2026

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540

Jan 14, 2026

Daily Field Report

T&R Restore

5307131522

Weather



38°F

8 AM

Precipitation: 0.0"

Wind: 2 mph

Humidity: 97%



46°F

12 PM

Precipitation: 0.0"

Wind: 2 mph

Humidity: 100%



55°F

5 PM

Precipitation: 0.0"

Wind: 2 mph




Humidity: 75%

Source: Weather

Progress Summary

Collected cuttings

ADDITIONAL PHOTOS

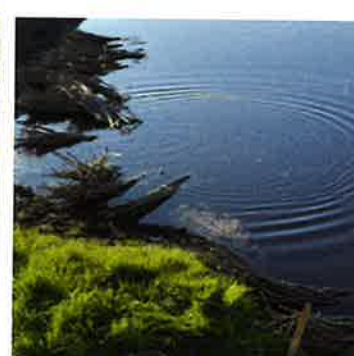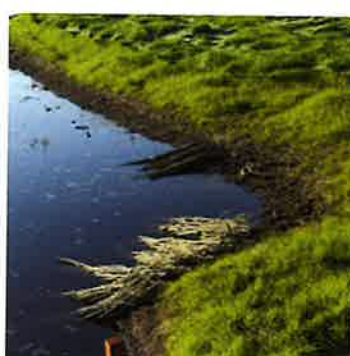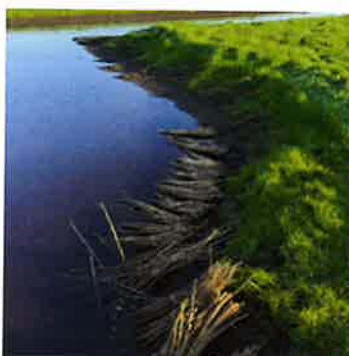

Employee Summary

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

21:04

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:29 AM - 4:00 PM	8:01
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:30 AM - 1:06 PM 2:25 PM - 4:00 PM	6:41
Vincent Ferrara	Yes	No	Yes	(-0:30) 9:08 AM - 4:00 PM	6:22

Cost Code Summary

Cost Code	Hours
2540 - Labor	14:23
2540 - Off Site Labor	6:41

Equipment Summary

NO DATA

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	14:23
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	6:41

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/14/2026

Prepared by: Nicholas Reynoso

01/14/2026 @ 4:08 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 29, 2026

Daily Field Report
T&R Restore
5307131522

Weather



39°F

Precipitation: 0.0"
Wind: 1 mph
Humidity: 96%

8 AM



53°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 81%

12 PM



56°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 75%

5 PM

Source: Weather

Progress Summary

Planted cuttings collected cuttings a

ADDITIONAL PHOTOS



Employee Summary

5 contract labors onsite

EMPLOYEES ON SITE

6

INJURIES REPORTED

0

HOURS

34:10

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Contract Laborer	---	---	---	12:00 AM* - 12:30 AM	0:30
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:05 AM - 1:00 PM 1:00 PM - 3:30 PM	7:55
Katie Jacobs	Yes	No	Yes	10:00 AM - 12:00 PM	2:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:05 AM - 3:30 PM	7:55
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:05 AM - 3:30 PM	7:55
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:05 AM - 3:30 PM	7:55

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	32:10
2540 - Mgmt. ---	2:00

Equipment Summary

MACHINES ON SITE

2

TOTAL HOURS

15:50

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM	Josue Joan Valadez, Josue Joan Valadez	7:55	---	7:55
2024 F250	Luis Velasquez	7:55	---	7:55

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	2:30
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	31:40


Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/29/2026

Prepared by: Nicholas Reynoso

01/29/2026 @ 3:35 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540

Jan 22, 2026

Daily Field Report

T&R Restore

5307131522

Weather



42°F

Precipitation: 0.0"

Wind: 3 mph

Humidity: 100%

8 AM



55°F

Precipitation: 0.0"

Wind: 5 mph

Humidity: 80%

12 PM



56°F

Precipitation: 0.0"

Wind: 3 mph

Humidity: 72%

5 PM

Source:  Weather

Progress Summary

Augered holes planted cuttings

ADDITIONAL PHOTOS



Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

24:05

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00
Nicholas Reynoso	Yes	No	Yes	7:25 AM - 8:30 AM 8:30 AM - 9:05 AM (-0:30) 9:05 AM - 4:00 PM	8:05
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:25 AM - 3:55 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	23:30
2540 - Off Site Labor ---	0:35

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	8:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM	Josue Joan Valadez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	24:05

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/22/2026

Prepared by: Nicholas Reynoso

01/22/2026 @ 4:09 PM

Generated by:



www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 21, 2026

Daily Field Report
T&R Restore
5307131522

Weather



43°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 98%

8 AM



44°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 98%

12 PM



50°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 83%

5 PM

Source: Apple Weather

Progress Summary

Augered holes planted cuttings and collected cuttings

ADDITIONAL PHOTOS



Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

26:05

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	7:30 AM - 11:40 AM (-0:30) 11:40 AM - 4:00 PM	8:00
Katie Jacobs	Yes	No	Yes	(-0:30) 11:00 AM - 1:30 PM	2:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:25 AM - 4:00 PM	8:05
Vincent Ferrara	Yes	No	Yes	7:30 AM - 11:40 AM (-0:30) 11:40 AM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	24:05
2540 - Mgmt. ---	2:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	4:10

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM ---	Josue Joan Valadez	4:10	---	4:10

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	7:40
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	18:25

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/21/2026

Prepared by: Nicholas Reynoso

01/21/2026 @ 4:04 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540

Jan 20, 2026

Daily Field Report

T&R Restore

5307131522

Weather



42°F

Precipitation: 0.0"

Wind: 2 mph

Humidity: 99%

8 AM



45°F

Precipitation: 0.0"

Wind: 3 mph

Humidity: 98%

12 PM



47°F

Precipitation: 0.0"

Wind: 3 mph

Humidity: 94%

5 PM

Source: Weather

Progress Summary

Auger holes and planted cuttings

ADDITIONAL PHOTOS



Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE**4****INJURIES REPORTED****0****HOURS****21:20**

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	7:30 AM - 9:00 AM	1:30
Luis Velasquez	Yes	No	Yes	7:30 AM - 11:15 AM	3:45
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:25 AM - 4:00 PM	8:05
Vincent Ferrara	No	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	21:20

Equipment Summary

MACHINES ON SITE**3****TOTAL HOURS****13:20**

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM	Josue Joan Valadez	1:30	---	1:30
2022 Chevrolet	Nicholas Reynoso	8:05	---	8:05
2024 F250	Luis Velasquez	3:45	---	3:45

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	3:45
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	17:35

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---



Nicholas Reynoso

01/21/2026

Prepared by: Nicholas Reynoso

01/21/2026 @ 9:03 AM

Generated by:



www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 16, 2026

Daily Field Report
T&R Restore
5307131522

Weather



40°F

Precipitation: 0.0"
Wind: 1 mph
Humidity: 99%

8 AM



47°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 99%

12 PM



57°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 77%


5 PM

Source: Apple Weather

Progress Summary

Started to auger holes then sprayed understory added boards to drains

ADDITIONAL PHOTOS

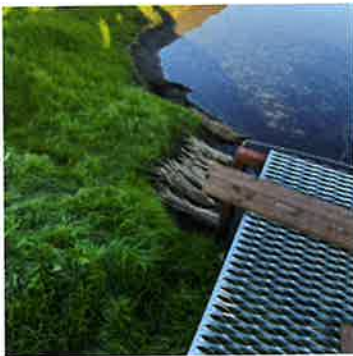

Employee Summary

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

22:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Luis Velasquez	Yes	No	Yes	7:30 AM - 8:37 AM 8:37 AM - 9:55 AM (-0:30) 9:55 AM - 2:34 PM 2:34 PM - 4:00 PM	8:00
Nicholas Reynoso	Yes	No	Yes	7:30 AM - 8:37 AM 8:37 AM - 9:55 AM (-0:30) 9:55 AM - 2:32 PM 2:32 PM - 2:45 PM 2:45 PM - 3:43 PM 3:43 PM - 4:00 PM	8:00
Vincent Ferrara	Yes	No	Yes	(-0:30) 10:00 AM - 5:00 PM	6:30

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	12:54
2540 - Off Site Labor ---	3:06
2540-Operator ---	6:30

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
2	14:30

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250 ---	Luis Velasquez, Luis Velasquez, Luis Velasquez, Luis Velasquez	8:00	---	8:00
New Side x Side POLARIS XPEDITION	Vincent Ferrara	6:30	---	6:30

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	1:26
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	14:34
2540-SHC5-Weed Management – Year 1	6:30

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/16/2026

Prepared by: Nicholas Reynoso

01/16/2026 @ 7:16 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Daily Field Report
T&R Restore
5307131522

Project #: 2540
Jan 15, 2026

Weather



39°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 98%

8 AM



50°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 96%

12 PM



56°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 80%

5 PM

Source: Apple Weather

Progress Summary

Collected cuttings and started to spray understory

ADDITIONAL PHOTOS



Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

28:27

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00
Luis Velasquez	Yes	No	Yes	7:29 AM - 11:16 AM (-0:30) 11:16 AM - 12:49 PM 12:49 PM - 4:01 PM	8:02
Nicholas Reynoso	Yes	No	Yes	(-0:07) 7:29 AM - 12:07 PM 2:32 PM - 4:00 PM	5:59
Vincent Ferrara	Yes	No	Yes	9:03 AM - 12:07 PM (-0:30) 12:08 PM - 4:00 PM	6:26

Cost Code Summary

Cost Code	Hours
2540 - Labor	12:07
2540 - Off Site Labor	9:11

2540-Operator

3:22

2540-Transportation

3:47

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
4	19:23

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
150 Gallon Sprayer	Luis Velasquez	---	3:47	3:47
2024 F250	Luis Velasquez, Luis Velasquez, Luis Velasquez	8:02	---	8:02
Gooseneck Trailer	Luis Velasquez	---	3:47	3:47
Side-by-side POLARIS XPEDITION	Luis Velasquez	---	3:47	3:47

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	12:07
2540-SHC1-Item 2 Site Preparation	3:47
2540-SHC1-Item 3 Irrigation Installation	3:12
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	5:59
2540-SHC5-Weed Management – Year 1	3:22

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---



Nicholas Reynoso

01/15/2026

Prepared by: Nicholas Reynoso

01/15/2026 @ 4:03 PM

Generated by:



www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 30, 2026

Daily Field Report
T&R Restore
5307131522

Weather



41°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 97%

8 AM



51°F

Precipitation: 0.0"
Wind: 4 mph
Humidity: 93%

12 PM



57°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 78%

5 PM

Source: Weather

Progress Summary

Collected cuttings and planted cuttings

ADDITIONAL PHOTOS



Employee Summary

5 contract labors onsite

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

31:50

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:05 AM - 3:35 PM	8:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:05 AM - 3:30 PM	7:55
Nicholas Reynoso	Yes	No	Yes	7:05 AM - 9:35 AM 9:35 AM - 10:35 AM (-0:30) 10:35 AM - 3:30 PM	7:55
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:05 AM - 3:35 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	31:50

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	7:55

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250	Luis Velasquez	7:55	---	7:55

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	1:00
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	30:50

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/30/2026

Prepared by: Nicholas Reynoso

01/30/2026 @ 3:44 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 23, 2026

Daily Field Report
T&R Restore
5307131522

Weather



43°F

8 AM

Precipitation: 0.0"
Wind: 3 mph
Humidity: 99%



46°F

12 PM

Precipitation: 0.0"
Wind: 3 mph
Humidity: 98%



48°F

5 PM


Precipitation: 0.0"
Wind: 2 mph
Humidity: 93%

Source: Apple Weather

Progress Summary

Augered holes planted cuttings and collected cuttings

ADDITIONAL PHOTOS

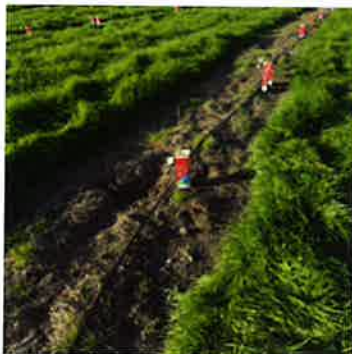

Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE

5

INJURIES REPORTED

0

HOURS

34:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Josue Joan Valadez	Yes	No	Yes	(-0:30) 7:35 AM - 1:05 PM 1:05 PM - 4:05 PM	8:00
Katie Jacobs	Yes	No	Yes	1:00 PM - 3:30 PM	2:30
Nicholas Reynoso	Yes	No	Yes	7:40 AM - 8:50 AM 8:50 AM - 9:15 AM (-0:25) 9:15 AM - 12:25 PM (-0:05) 12:25 PM - 4:10 PM	8:00
Tessa Reynoso	Yes	No	Yes	(-0:30) 7:00 AM - 3:30 PM	8:00
Vincent Ferrara	No	No	Yes	(-0:30) 7:30 AM - 1:00 PM 1:00 PM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	19:55

2540 - Mgmt.	2:30
--------------	------

2540 - Off Site Labor	4:05
-----------------------	------

2540-Administrative	8:00
---------------------	------

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	8:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2021 RAM	Josue Joan Valadez, Josue Joan Valadez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	6:00
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	18:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/24/2026

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540

Jan 26, 2026

Daily Field Report

T&R Restore

5307131522

Weather



41°F

Precipitation: 0.0"

Wind: 2 mph

Humidity: 98%

8 AM



50°F

Precipitation: 0.0"

Wind: 4 mph

Humidity: 80%

12 PM



56°F

Precipitation: 0.0"

Wind: 2 mph

Humidity: 70%

5 PM

Source:  Weather

Progress Summary

Collecting cuttings and augered holes

ADDITIONAL PHOTOS



Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

18:10

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Katie Jacobs	Yes	No	Yes	(-0:30) 11:00 AM - 1:30 PM	2:00
Luis Velasquez	Yes	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00
Nicholas Reynoso	Yes	No	Yes	7:25 AM - 7:35 AM (-0:30) 7:35 AM - 4:05 PM	8:10

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	8:10
2540 - Mgmt. ---	2:00
2540 - Off Site Labor ---	8:00

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	8:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250	Luis Velasquez	8:00		8:00

Subproject Summary

Subprojects	Hours
2540 - EX Additional Planting	2:00
2540-Off-Site work Cuttings	8:00
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	8:10

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/26/2026

Prepared by: Nicholas Reynoso

01/26/2026 @ 6:59 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 19, 2026

Daily Field Report
T&R Restore
5307131522

Weather



41°F

Precipitation: 0.0"
Wind: 4 mph
Humidity: 99%

8 AM



45°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 98%

12 PM



51°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 85%

5 PM

Source: Apple Weather

Progress Summary

- Spraying centers
- Drilling
- Pump setup

ADDITIONAL PHOTOS



Employee Summary

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

22:30

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Luis Velasquez	Yes	No	Yes	7:50 AM - 10:00 AM (-0:30) 10:00 AM - 4:20 PM	8:00
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:50 AM - 4:20 PM 7:50 AM - 7:50 AM	8:00
Vincent Ferrara	Yes	No	Yes	(-0:30) 10:00 AM - 5:00 PM	6:30

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	16:00
2540-Operator ---	6:30

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
2	14:30

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250	Luis Velasquez, Luis Velasquez	8:00	---	8:00
New Side x Side POLARIS XPEDITION	Vincent Ferrara	6:30	---	6:30

Subproject Summary

Subprojects	Hours
2540-SHC1-Item 3 Irrigation Installation	5:50
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	10:10
2540-SHC5-Weed Management – Year 1	6:30

Herbicide Usage

Aqua master
Patrol

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Vincent Ferrara

01/19/2026

Prepared by: Vincent Ferrara

01/19/2026 @ 5:02 PM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 27, 2026

Daily Field Report
T&R Restore
5307131522

Weather



38°F

Precipitation: 0.0"
Wind: 2 mph
Humidity: 100%

8 AM



47°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 93%

12 PM



49°F

Precipitation: 0.0"
Wind: 1 mph
Humidity: 90%

5 PM

Source: Apple Weather

Progress Summary

Augered holes collected cuttings and unloaded plants

ADDITIONAL PHOTOS



Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE

3

INJURIES REPORTED

0

HOURS

24:05

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Luis Velasquez	Yes	No	Yes	(-0:30) 7:00 AM - 12:30 PM 12:30 PM - 3:30 PM	8:00
Nicholas Reynoso	Yes	No	Yes	6:55 AM - 7:05 AM (-0:30) 7:05 AM - 12:35 PM 12:35 PM - 3:30 PM	8:05
Vincent Ferrara	Yes	No	Yes	(-0:30) 7:00 AM - 12:30 PM 12:30 PM - 3:30 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor ---	21:00
2540 - Off Site Labor ---	3:05

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	8:00

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250	Luis Velasquez, Luis Velasquez	8:00	---	8:00

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	6:00
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	18:05

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/28/2026

Prepared by: Nicholas Reynoso

01/28/2026 @ 4:32 AM

Generated by:

 **BusyBusy**

www.busybusy.com

2540 - Twitchell Island Wetland Enhancement (TWERP)

Project #: 2540
Jan 28, 2026

Daily Field Report
T&R Restore
5307131522

Weather



46°F

Precipitation: 0.0"
Wind: 3 mph
Humidity: 98%

8 AM



57°F

Precipitation: 0.0"
Wind: 11 mph
Humidity: 82%

12 PM



59°F

Precipitation: 0.0"
Wind: 4 mph
Humidity: 73%

5 PM

Source:  Weather

Progress Summary

Collected cuttings Augered holes planted cuttings

ADDITIONAL PHOTOS



Employee Summary

3 contract labors onsite

EMPLOYEES ON SITE

4

INJURIES REPORTED

0

HOURS

57:05

Employee	Correct Time	Injured	Break Compliance	Entries	Hours
Contract Laborer	---	---	---	7:00 AM - 11:59 PM* 7:00 AM - 11:00 PM	33:00
Luis Velasquez	Yes	No	Yes	7:30 AM - 11:25 AM (-0:30) 11:25 AM - 4:05 PM	8:05
Nicholas Reynoso	Yes	No	Yes	(-0:30) 7:30 AM - 4:00 PM	8:00
Vincent Ferrara	Yes	No	Yes	7:30 AM - 11:35 AM (-0:30) 11:35 AM - 4:00 PM	8:00

Cost Code Summary

Cost Code	Hours
2540 - Labor	57:05

Equipment Summary

MACHINES ON SITE	TOTAL HOURS
1	8:05

Name	Operator	Labor Hrs	Add-On Hrs	Total Hrs
2024 F250	Luis Velasquez, Luis Velasquez	8:05	---	8:05

Subproject Summary

Subprojects	Hours
2540-Off-Site work Cuttings	8:00
2540-SHC3 Plant install (CF) item 1-7 Pole Cuttings	33:05
2540-SHC4 Plant install (DF) item 1-9 Container	16:00

Herbicide Usage

NO DATA

Herbicide

Question	Yes	No	N/A	Description
Rate	☐	☐	☐	---
Amount	☐	☐	☐	---

Sign-Off



Nicholas Reynoso

01/29/2026

Prepared by: Nicholas Reynoso

01/29/2026 @ 10:45 AM

Generated by:

 **BusyBusy**

www.busybusy.com

EXHIBIT C



Progress Pay Estimate

No. 3

PROJECT: 1110-1010-11
Twitchell Island
TWERP Plant Procurement

DATE: 2/10/2026

CONTRACTOR: The Watershed Nursery

CONTRACT ID: 1601-09-23-24-01

CONTRACT TIME:

Original Time 479 days
Notice to Proceed Date 9/23/2024
Original Completion Date 1/15/2026
Approved Time Extensions 16 days
Revised Completion Date 1/31/2026
Work Completed Through 1/31/2026
Elapsed Time 495 days
Percent Time Elapsed 100.0%

CONTRACT COST:

Original Contract Price \$119,839.91
Approved Change Orders (\$5,233.11)
Percent Change Orders -4.4%
Revised Contract Price \$114,606.80
Amount Complete to Date \$114,606.80
Percent Complete 100.0%

CURRENT PAYMENT SUMMARY:

DESCRIPTION	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
To Date	\$114,606.80	(\$5,730.34)	\$0.00	\$108,876.46
Previous	\$60,325.89	(\$3,016.29)	\$0.00	\$57,309.60
Current	\$54,280.91	(\$2,714.05)	\$0.00	\$51,566.86
Net Payment Due This Invoice:				\$51,566.86

OVERALL PAYMENT SUMMARY:

NO.	WORK COMPLETED THROUGH	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
1	10/31/2024	\$33,401.05	(\$1,670.05)	\$0.00	\$31,731.00
2	7/31/2025	\$26,924.84	(\$1,346.24)	\$0.00	\$25,578.60
3	1/31/2026	\$54,280.91	(\$2,714.05)	\$0.00	\$51,566.86
TOTALS:		\$114,606.80	(\$5,730.34)	\$0.00	\$108,876.46

NOTES:

--

SUPPORTING DOCUMENTATION

- The Watershed Nursery Invoice No. 2363 dated 2/10/2026.

RECOMMENDED FOR PAYMENT

KSN, Inc.

BY:

Erik Almaas, PE
Project Manager



KJELDSEN
SINNOCK
NEUDECK
CIVIL ENGINEERS & LAND SURVEYORS

PROJECT: 1110-1010-11
Twitchell Island
TWERP Plant Procurement

CONTRACTOR: The Watershed Nursery

Progress Pay Estimate No. 3

DATE: 2/10/2026

CONTRACT ID: 1601-09-23-24-01

ITEM NO.	ITEM DESCRIPTION	UNIT	CONTRACT			TOTAL ESTIMATE TO DATE			PREVIOUS ESTIMATE			CURRENT ESTIMATE			
			QTY	UNIT PRICE	AMOUNT	QTY	%	AMOUNT	QTY	%	AMOUNT	QTY	%	AMOUNT	
ORIGINAL CONTRACT															
SCHEDULE 1					\$119,839.91	100.00%		\$119,839.91	\$0.34%	\$60,325.89	49.66%	\$59,514.02			
					\$119,839.91	100.00%		\$119,839.91	\$0.34%	\$60,325.89	49.66%	\$59,514.02			
1	Acer negundo	EA	515	\$11.82	\$6,087.30	515.00	100.00%	\$6,087.30	259.24	50.34%	\$3,064.27	255.76	49.66%	\$3,023.03	
2	Baccharis pilularis	EA	4,393	\$9.83	\$43,084.89	4,393.00	100.00%	\$43,084.89	2,206.35	50.34%	\$21,688.39	2,176.65	49.66%	\$21,396.50	
3	Cephalanthus occidentalis	EA	1,206	\$9.83	\$11,854.98	1,206.00	100.00%	\$11,854.98	607.09	50.34%	\$5,967.65	598.91	49.66%	\$5,887.33	
4	Faxinus latifolia	EA	483	\$11.82	\$5,709.06	483.00	100.00%	\$5,709.06	243.14	50.34%	\$2,873.87	239.86	49.66%	\$2,835.19	
5	Platanus racemosa	EA	1,231	\$11.82	\$14,550.42	1,231.00	100.00%	\$14,550.42	619.67	50.34%	\$7,324.50	611.33	49.66%	\$7,225.92	
6	Rosa californica	EA	1,410	\$9.83	\$13,860.30	1,410.00	100.00%	\$13,860.30	709.78	50.34%	\$6,977.10	700.22	49.66%	\$6,883.20	
7	Rubus ursinus	EA	450	\$9.83	\$4,423.50	450.00	100.00%	\$4,423.50	226.52	50.34%	\$2,226.73	223.48	49.66%	\$2,196.77	
8	Sambucus mexicana	EA	1,788	\$9.83	\$17,576.04	1,788.00	100.00%	\$17,576.04	900.06	50.34%	\$8,847.56	887.94	49.66%	\$8,728.48	
9	Vitis californica	EA	274	\$9.83	\$2,693.42	274.00	100.00%	\$2,693.42	137.93	50.34%	\$1,355.83	136.07	49.66%	\$1,337.59	
CHANGE ORDERS					(\$2,233.11)	100.00%		(\$2,233.11)	0.00%	\$0.00	100.00%			(\$2,233.11)	
CO-001					(\$2,233.11)	100.00%		(\$2,233.11)	0.00%	\$0.00	100.00%			(\$2,233.11)	
001-001	Delivery Credit	LS	1	(\$2,304.27)	(\$2,304.27)			(\$2,304.27)						(\$2,304.27)	
002-001	Acer negundo	EA	240	\$11.82	\$2,836.80	240	100.00%	\$2,836.80				240	100.00%	\$2,836.80	
002-002	Cephalanthus occidentalis	EA	-126	\$9.83	(\$1,238.58)	-126	100.00%	(\$1,238.58)				-126	100.00%	(\$1,238.58)	
002-003	Platanus racemosa	EA	-383	\$11.82	(\$4,527.06)	-383.0	100.00%	(\$4,527.06)				-383.0	100.00%	(\$4,527.06)	
TOTALS:					\$114,606.80	100.00%		\$114,606.80	52.64%	\$60,325.89	47.36%		\$54,280.91		

**Watershed Nursery Cooperative Corporation**

601 Canal Blvd Ste A
Richmond, CA 94804 USA
5102342222
maribel@thewatershednursery.com

INVOICE

BILL TO

Kjeldsen, Sinnock, Neudeck,
Inc

INVOICE # 2363**DATE 02/10/2026****DUE DATE 03/12/2026****TERMS Net 30****PROJECT**

TWERP

	DESCRIPTION	QTY	RATE	AMOUNT
	Contract No. 1601-09-23-2401			
Plants Contract	Final Payment on plant Material. Total amount \$ 86,304.36 Deposit paid \$ 44,258.20	1	42,046.16	42,046.16T
Propagule Collecting	Final payment on Collection- Deposit paid \$ 2,196.00	0.50	4,392.00	2,196.00
Project Management	Final payment on Project Management Deposit paid \$ 3,799.50	0.50	7,599.00	3,799.50
Delivery	Delivery- 11/25/25, 12/03/25, 02/03/26	3	941.00	2,823.00

Thank you for you business !

Please remember that containers must be returned within 60 days of receipt of plants to receive container deposit refund. Return must be coordinated with nursery staff

SUBTOTAL	50,864.66
TAX	3,416.25
TOTAL	54,280.91
BALANCE DUE	\$54,280.91

EXHIBIT D



Progress Pay Estimate

No. 4

RELEASE OF RETENTION

PROJECT: 1110-1010-11
Twitchell Island
TWERP Plant Procurement

DATE: 2/10/2026

CONTRACTOR: The Watershed Nursery

CONTRACT ID: 1601-09-23-24-01

CONTRACT TIME:

Original Time 479 days
Notice to Proceed Date 9/23/2024
Original Completion Date 1/15/2026
Approved Time Extensions 16 days
Revised Completion Date 1/31/2026
Work Completed Through 1/31/2026
Elapsed Time 495 days
Percent Time Elapsed 100.0%

CONTRACT COST:

Original Contract Price \$119,839.91
Approved Change Orders (\$5,233.11)
Percent Change Orders -4.4%
Revised Contract Price \$114,606.80
Amount Complete to Date \$114,606.80
Percent Complete 100.0%

CURRENT PAYMENT SUMMARY:

DESCRIPTION	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
To Date	\$114,606.80	\$0.00	\$0.00	\$114,606.80
Previous	\$114,606.80	(\$5,730.34)	\$0.00	\$108,876.46
Current	\$0.00	\$5,730.34	\$0.00	\$5,730.34
Net Payment Due This Invoice:				\$5,730.34

OVERALL PAYMENT SUMMARY:

NO.	WORK COMPLETED THROUGH	TOTAL EARNINGS	LESS 5% RETENTION	LESS DEDUCTIONS	NET EARNINGS
1	10/31/2024	\$33,401.05	(\$1,670.05)	\$0.00	\$31,731.00
2	7/31/2025	\$26,924.84	(\$1,346.24)	\$0.00	\$25,578.60
3	1/31/2026	\$54,280.91	(\$2,714.05)	\$0.00	\$51,566.86
4	RETENTION	\$0.00	\$5,730.34	\$0.00	\$5,730.34
TOTALS:		\$114,606.80	\$0.00	\$0.00	\$114,606.80

NOTES:

Release of retention.

SUPPORTING DOCUMENTATION

RECOMMENDED FOR PAYMENT

KSN, Inc.

BY:


Erik Almaas, PE
Project Manager

EXHIBIT E

FILE SPEC: P:\1110_Twitchell_Island\0950_Pump_Station_Solar_Array\08_Civil\400_Plans\020_CAD\Sheets_Transformer_Platform_Updated\260211_C-101_5to1.dwg
PLOT DATE: Feb 11, 2026 - 3:46pm



FILL AND AB QUANTITIES	
FILL QUANTITY	±530 CY
AGGREGATE BASE QUANTITY	160 TNS



KJELDEN SINNOCK NEUDECK
INC.
CIVIL ENGINEERS & LAND SURVEYORS
www.ksninc.com
711 N Pershing Avenue
Stockton, CA 95203
209-946-0268
1550 Harbor Drive, Suite 212
West Sacramento, CA 95691
916-403-5900

RECLAMATION DISTRICT 1601
TWITCHELL ISLAND
PUMP STATION SOLAR ARRAY TRANSFORMER
SITE PLAN

DRAWING SCALE
1" = 10'
ORIGINAL DRAWING SCALE
0 1/2" 1"
[Scale bar]


EXHIBIT NO.
A
PAGE NO.
1

FILE SPEC: P:\1110_TwitchellIsland\0950_Pump_Station_Solar_Array\08_Civil\400_Plans\020_CAD\Sheets_Transformer_Platform_Updated\260211_C-101_5101.dwg
PLOT DATE: Feb 11, 2026 - 3:46pm




NOTES

1. PROVIDE CAST-IN ANCHOR SLEEVES OR INSERTS OUTSIDE OF CONDUIT BLOCKOUT AREAS. FINAL ANCHOR LOCATIONS SHALL BE COORDINATED WITH ABB INSTALLATION REQUIREMENTS AND ELECTRICAL SHOP DRAWINGS.
2. CONDUIT BLOCKOUT LOCATIONS SHOWN ARE NOMINAL. MINOR ADJUSTMENTS PERMITTED TO SUIT PRECAST FABRICATION AND FIELD CONDUIT ALIGNMENT. FINAL BLOCKOUT LOCATIONS SHALL BE COORDINATED WITH ABB INSTALLATION REQUIREMENTS AND ELECTRICAL SHOP DRAWINGS. AFTER CONDUIT INSTALLATION, GROUT ALL UNUSED BLOCKOUTS AND ANNULAR SPACES AROUND CONDUITS FLUSH WITH PAD SURFACE USING NON-SHRINK GROUT OR APPROVED EQUIVALENT.
3. PRECAST PAD SHALL REMAIN CONTINUOUS; DO NOT SAW-CUT OR REMOVE CONCRETE EXCEPT AT FORMED OR APPROVED CORE-DRILLED CONDUIT OPENINGS.
4. LIMITED FIELD CORE-DRILLING OF PRECAST PAD IS PERMITTED FOR MINOR STUB-UP ADJUSTMENTS, SUBJECT TO ENGINEER'S APPROVAL. SAW-CUTTING OF LONG SLOTS OR TRENCHES IS NOT PERMITTED.
5. PROVIDE POSITIVE DRAINAGE AT PAD SURFACE; FINISH PAD TOP FLUSH AND SLOPED AS REQUIRED TO PREVENT WATER PONDING AT EQUIPMENT BASE.

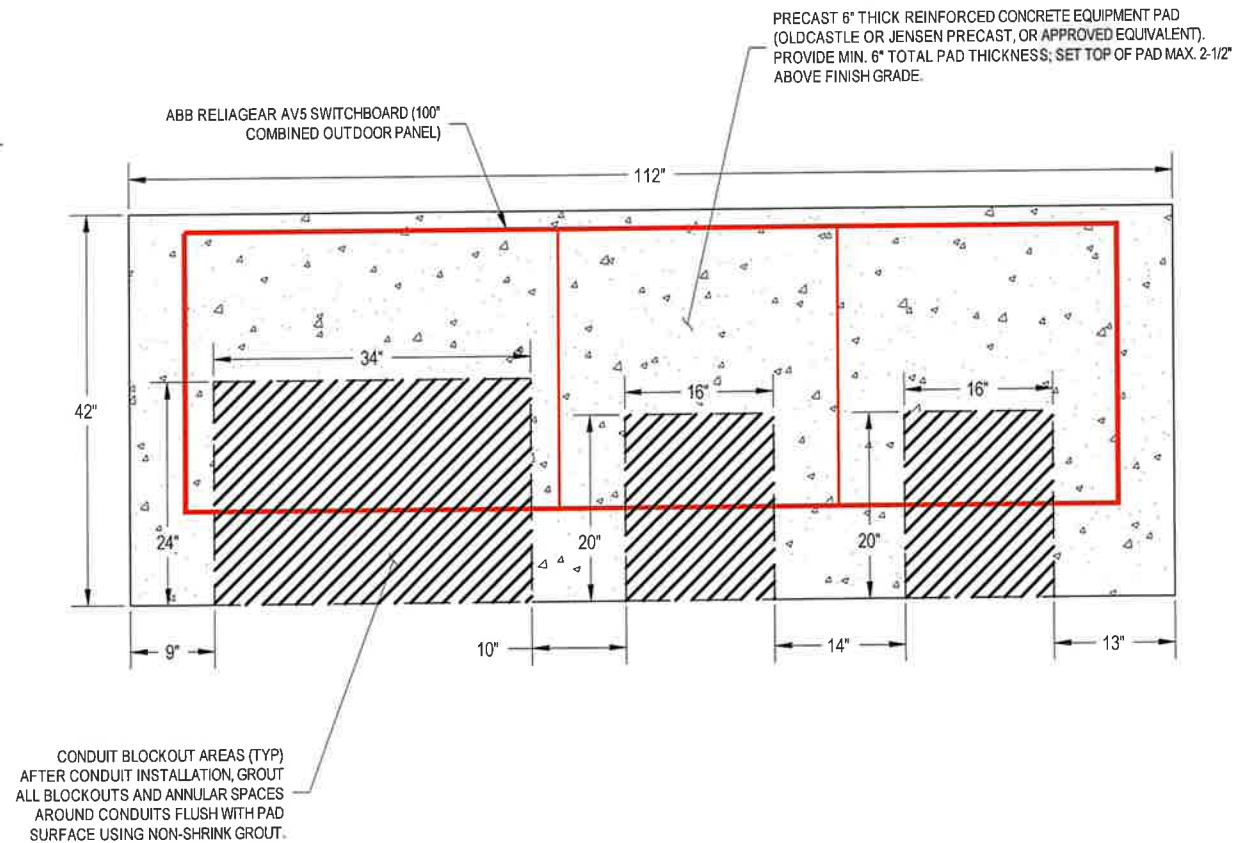

1 SWITCHBOARD PAD DETAIL
SCALE: 1" = 10'

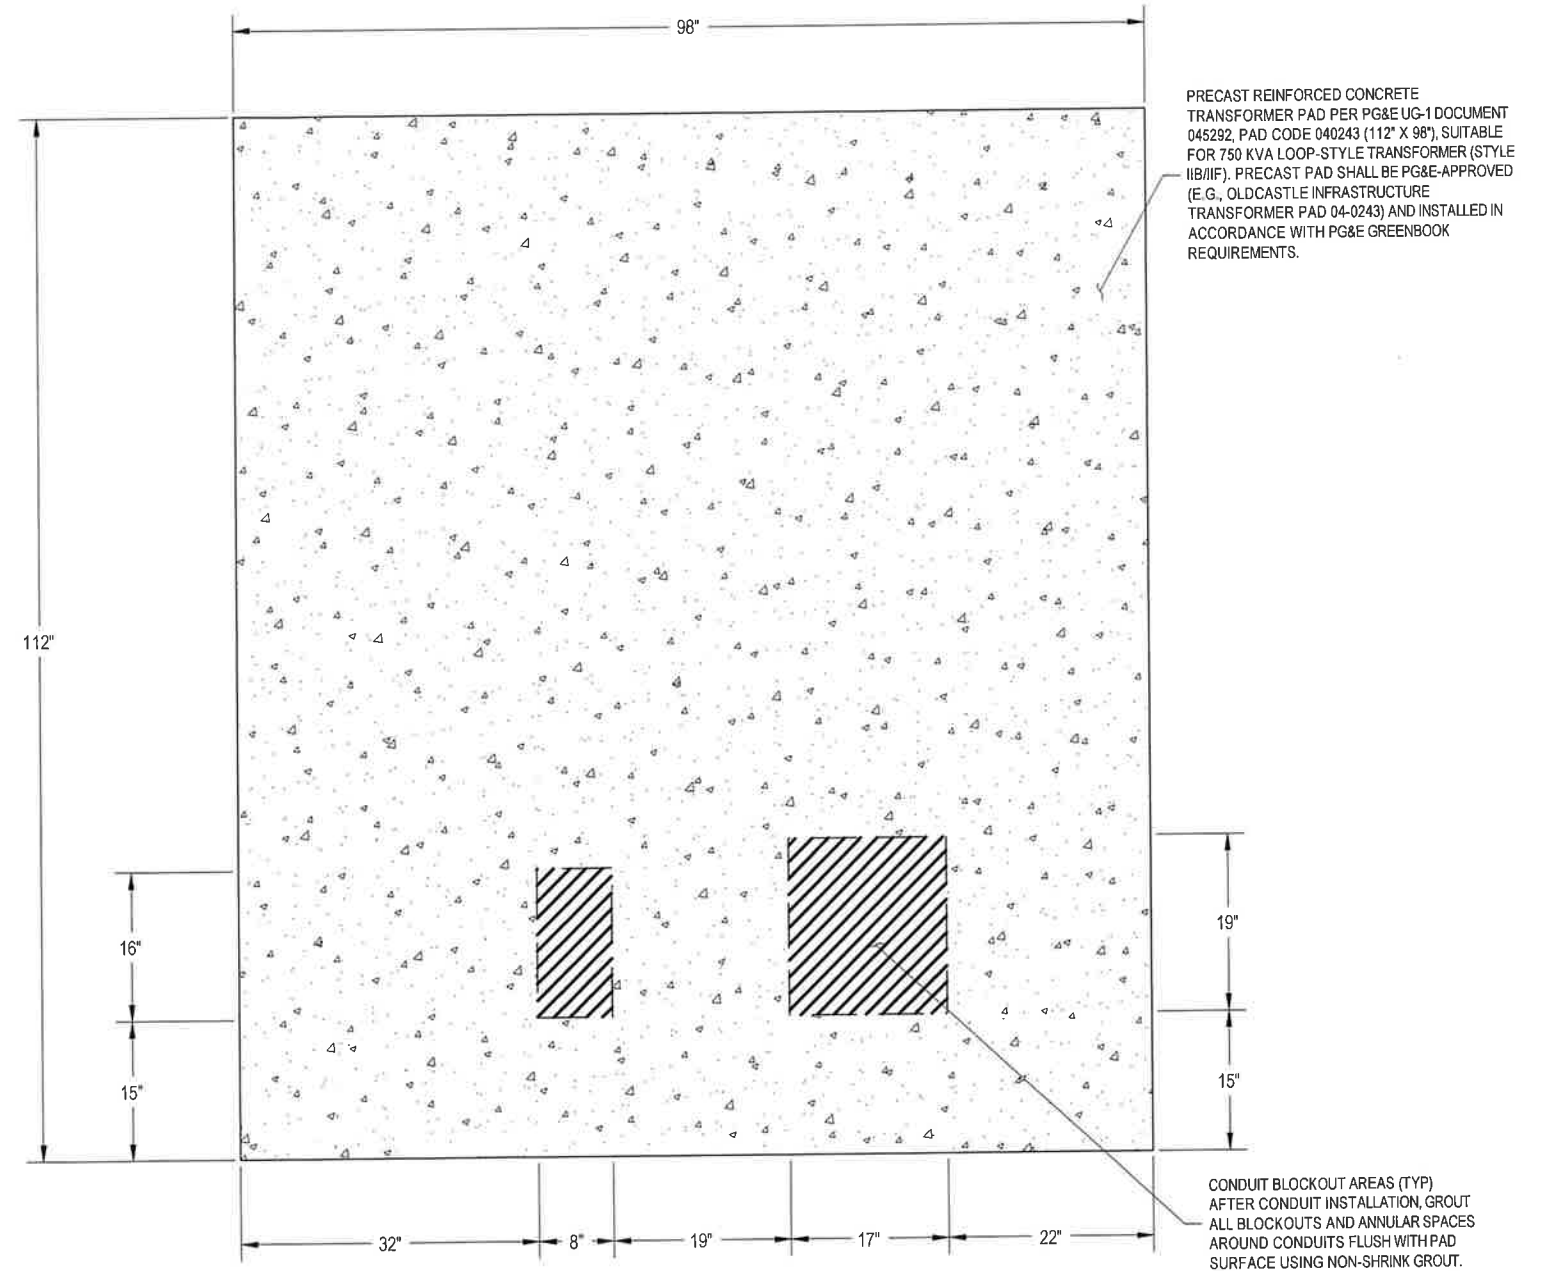

2 TRANSFORMER PAD DETAIL
SCALE: 1" = 10'

KSN INC.
KJELSEN SINNOCK NEUDECK
CIVIL ENGINEERS & LAND SURVEYORS
www.ksninc.com
711 N Pershing Avenue
Stockton, CA 95203
209-946-0268
1550 Harbor Drive, Suite 212
West Sacramento, CA 95691
916-403-5900

RECLAMATION DISTRICT 1601
TWITCHELL ISLAND
PUMP STATION SOLAR ARRAY TRANSFORMER
DETAILS

DRAWING SCALE
AS SHOWN
ORIGINAL DRAWING SCALE
0 1/2" 1"
[Scale bar]

EXHIBIT NO.
A
PAGE NO.
2
